

Instawards Statement of Work (SOW) 30-Day Scoped Engagement

1. Project & Team Information

Project Name:	RAÍZ (Protocolo Raíz)
Builder / Team Name:	RAÍZ — Juan Pablo Conrado Molina (smart contracts / backend / Android) & Diana Sofía Durán Samacá (product / design)
Primary Contact (Name + Email):	Juan Pablo Conrado Molina — conradom.juan@javeriana.edu.co
Ambassador Chapter:	Colombia Chapter
Ambassador Chapter Lead:	Laura Estupiñán
Date Submitted:	July 15, 2026
Suggested Sprint Start Date:	July 20, 2026

2. Instawards Overview & Intent

2.1 Instawards Purpose (for Builder Context)

Instawards are designed to support short, clearly scoped, execution-focused work that helps a project make tangible progress toward building on Stellar. Instawards are meant to fund specific, achievable outcomes that can be completed and demonstrated within 30 days or less.

This SOW represents a shared commitment between the Builder and the Ambassador Chapter Lead on what will be delivered, why it matters, and how success will be verified.

3. Problem Statement & Objective

Problem Being Addressed	What specific problem, gap, or blocker is this Instaward intended to solve?	RAÍZ won the Stellar PULSO Hackathon (Bogotá, July 2026) with a fully functional MVP on Stellar testnet: 4 Soroban smart contracts, a native Android app, DeFindex yield integration and passkey smart wallets, all verified end-to-end on real devices. Three specific gaps block the path to production: (1) the demo admin key is embedded in the APK, so admin operations (merchant registration, resident minting, faucet) cannot ship as-is — our declared mainnet blocker; (2) governance executions record a deterministic placeholder hash instead of linking to the real Stellar transaction, weakening our
--------------------------------	---	---

Instawards Statement of Work (SOW)
30-Day Scoped Engagement

		core transparency promise; (3) the fiat on-ramp is simulated with an admin faucet instead of a real SEP-24 anchor flow.
Objective of This Instaward	In one or two sentences, what will be true at the end of 30 days if this Instaward is successful?	At the end of 30 days RAÍZ will be production-ready at the protocol level: a public, open-source admin relay replaces all embedded secrets in the APK; every governance execution links to its real, verifiable Stellar transaction on Stellar Expert; and users can complete a SEP-10 + SEP-24 deposit flow against the SDF testnet anchor from inside the app.
Example prompts for builders: What is currently preventing progress? What is unclear, missing, or unbuilt today? Why is this problem worth solving now?		

4. Scope of Work (30-Day Deliverables)

Important guidance: This scope must be achievable within **30 calendar days**. If the work feels larger, it should be reduced or split into more achievable phases.

4.1 In-Scope Deliverables

Deliverable	Description (What will be built or produced?)	Why this matters
D1 — Admin Relay Service	Open-source backend service that signs admin operations server-side — merchant registration, resident minting and the test-USDC faucet — replacing the demo admin key currently embedded in the Android APK. Includes deployment of the service and migration of the app to consume it, producing a new release APK that contains zero secrets.	It is our declared mainnet blocker: no production release is possible while admin secrets ship inside the APK.
D2 — Real Transaction Linking in the Transparency Dashboard	Every governance Execution in the transparency dashboard links to its real Stellar transaction: the client captures the transaction hash from the RPC result and correlates on-chain execution events, replacing the current deterministic placeholder hash.	Verifiable transparency is RAÍZ's core promise: every community-fund execution becomes auditable by anyone on Stellar Expert in one click.

Instawards Statement of Work (SOW) 30-Day Scoped Engagement

D3 — SEP-10 + SEP-24 On-Ramp (Testnet Anchor)	SEP-10 authentication and the SEP-24 interactive deposit flow integrated in the Android app against the SDF testnet anchor, replacing the simulated admin faucet as the USDC on-ramp.	It proves the real fiat-to-USDC path tourists in LatAm will use, and de-risks the future integration with production anchors (MoneyGram, Anclap).
Out-of-Scope (Explicitly Not Included) List anything that might be assumed but is not included in this Instaward scope.		
Mainnet deployment; SEP-12 KYC for residents; real-money fiat rails / production anchors; IPFS for reward images; iOS app; contract security audit; new product features. These belong to the next phase (SCF Build application).		

4.2 Deliverable-Aligned Budget Request

Requested Budget Amount	Rationale for Budget Request
USD 5,000 (paid in XLM)	Deliverable-aligned budget covering ~155 hours of development ($\approx$ one month full-time): • D1 — Admin relayer: 75 h (backend design, server-side signing, endpoints, deployment, app migration) — USD 2,300 • D2 — Real tx linking: 20 h (hash capture via RPC, event correlation, dashboard UI) — USD 600 • D3 — SEP-10/24 integration: 45 h (auth, interactive deposit flow, state handling) — USD 1,400 • Infrastructure & tooling: relayer VPS (3 months), domain, AI development assistant, certificates — USD 300 • QA & evidence: 15 h (physical-device testing, docs, demo video, evidence package) — USD 400

5. 30-Day Execution Plan & Timeline

5.1 Weekly Breakdown

Week	Planned Work	Expected Output

Instawards Statement of Work (SOW)
30-Day Scoped Engagement

Week 1	Admin relayer: architecture and authorization model; backend implementation with server-side signing; endpoints for merchant registration, resident minting and faucet; deploy the service to testnet infrastructure.	Relayer service live against testnet, with a public open-source repository.
Week 2	Migrate the Android app to the relayer; remove all admin secrets from BuildConfig; produce a release APK; regression-test the three admin flows on physical devices.	D1 complete: release APK with zero embedded secrets, verifiable by decompilation.
Week 3	Real transaction linking: capture tx hash from RPC results, correlate on-chain execution events, dashboard UI with Stellar Expert links. Begin SEP-10 authentication against the SDF testnet anchor.	D2 complete: every execution links to its real Stellar transaction. SEP-10 auth working.
Week 4	Complete the SEP-24 interactive deposit flow in-app; buffer for testnet flakiness; documentation sync, demo video and evidence package.	D3 complete: SEP-24 deposit demonstrated end-to-end. Full evidence package delivered.

6. Evidence of Completion (Required)

Important guidance: Evidence should be clear, verifiable, and easy to review by the Ambassador Chapter Lead **with minimal technical expertise**.

6.1 Planned Evidence to Be Submitted

Deliverable	Evidence Type (link, repo, demo, screenshot, doc, tx hash, etc.)	Description
D1 — Admin Relayer	Repo link + release APK + verification doc + screenshots	Open-source relayer repository; downloadable release APK; 1-page “how to verify” doc showing the decompiled APK contains zero admin secrets.

Instawards Statement of Work (SOW)
30-Day Scoped Engagement

D2 — Real Tx Linking	Live dashboard + 3 direct Stellar Expert links	Screenshots of the transparency dashboard plus at least 3 governance executions, each linking to its real transaction on Stellar Expert — one click to verify.
D3 — SEP-10/24 On-Ramp	Demo video + tx hash	60-second video of a SEP-24 deposit completed end-to-end from the app against the SDF testnet anchor, plus the resulting transaction hash.

6.2 Evidence Verification Checklist (For Ambassador Use)

For each deliverable, the Ambassador Chapter Lead will assess whether evidence is present and sufficient.

Deliverable	Evidence Present	Evidence Partial	Evidence Missing	Comments
Deliverable 1	☐	☐	☐	
Deliverable 2	☐	☐	☐	
Deliverable 3	☐	☐	☐	

7. Next-Step Alignment

7.1 Anticipated Next Step After Completion

After this Instaward, the most likely next step is:

- ☒ Apply to SCF Build Award — this Instaward removes the three technical blockers to production; the next phase is a real-world pilot in a tourist neighborhood in Cartagena with a small group of merchants and residents, adding SEP-12 KYC, a security audit of

Instawards Statement of Work (SOW)

30-Day Scoped Engagement

the four contracts, and a local anchor for the fiat ramp. RAÍZ already ships a working DeFindex integration (SCF Integration Track partner).

- ☐ Continue development independently
- ☒ Apply for a follow-on Instaward (if eligible) — a second 30-day sprint (e.g. SEP-12 KYC groundwork and pilot preparation) while the SCF Build application is prepared and reviewed.
- ☐ Seek other ecosystem support
- ☐ Other:

8. Instawards Constraints Acknowledgement

By submitting this SOW, the Builder acknowledges:

- ☒ This scope will be completed within **30 days or less**.
- ☒ Instawards support execution, not open-ended exploration.
- ☒ A project may receive **no more than two follow-on Instawards**.
- ☒ Each Instaward is capped at **\$5,000**.
- ☒ Total Instawards funding may not exceed **\$15,000**.

9. Submission Confirmation

Once finalized, this Statement of Work will be submitted by the Ambassador Chapter Lead via the Instawards Airtable submission form for review and approval.

Instawards Statement of Work (SOW)
30-Day Scoped Engagement

Annex A — Sprint Plan & Verification Links

Everything below is public and verifiable in one click, without technical expertise.

A.1 — Verify the project (one click each)


- GitHub monorepo (contracts + Android app): https://github.com/JuanWimmin/Protocolo_Raiz
- Landing page with live on-chain data: <https://raizapp.xyz>
- Pitch deck (PULSO winner): <https://raizapp.xyz/pitch.html>
- Demo video (YouTube): <https://www.youtube.com/watch?v=y-9pplgVnnA>
- DoraHacks BUIDL page: <https://dorahacks.io/buidl/46112>
- On-chain resident verification tool: <https://raizapp.xyz/verificar-residente.html>
- Merchant & resident interviews (Drive):
https://drive.google.com/drive/folders/1vd_3RpL_2eZphFwEavG5rx7ZF3PYScdp
- Pool contract on Stellar Expert:
<https://stellar.expert/explorer/testnet/contract/CAKYU5HW5QPLAE5YBHH5L5P433VE3RMA7OGAZV2OQCSATD57TXEVN2FK>
- Governance contract on Stellar Expert:
<https://stellar.expert/explorer/testnet/contract/CAENXDX77SHDLNPXTQDV4M6W43SVHEJWOGOBQT5XHXPFE06PNB77PVE>
- Treasury contract on Stellar Expert:
<https://stellar.expert/explorer/testnet/contract/CDGGFSV74EGBEUQWLZ5OMQZJUPXBI7BYCNZJRMCGYEKZEPN3QBWQGPXA>
- Rewards contract on Stellar Expert:
<https://stellar.expert/explorer/testnet/contract/CD5OET7FPJAWPID5DCBYRHDJXNICXAPLAWDRDA3NCS5IIBACEW2I6PPT>
- DeFindex vault (community fund yield):
<https://stellar.expert/explorer/testnet/contract/CBMVK2JK6NTOT2O4HNQAIQFJY232BHKGLIMXDVQVHIIZKDACXDFZDWHN>

A.2 — The 30-day sprint at a glance

One deliverable lands per week; each deliverable ships with evidence a reviewer can check directly.

Instawards Statement of Work (SOW) 30-Day Scoped Engagement


30-day sprint - one deliverable lands each week, each with its own evidence

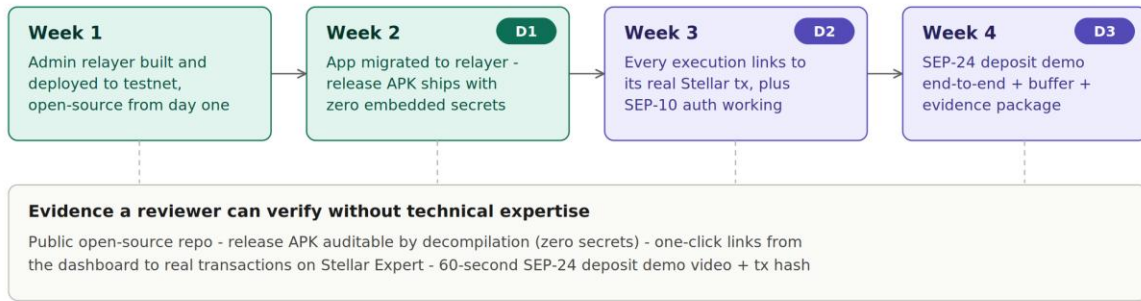

A.3 — D1 in one picture: removing the mainnet blocker

Today the demo admin key ships inside the APK. After the sprint, an open-source relayer signs admin operations server-side and the APK contains zero secrets.

D1 - Admin relayer: removing the mainnet blocker

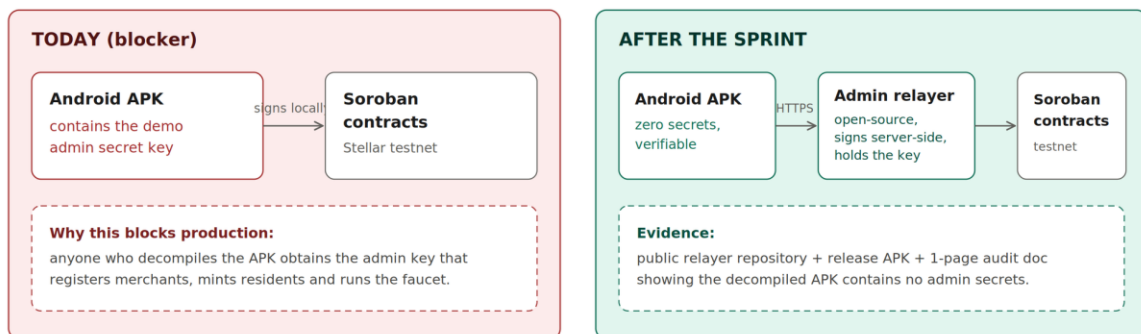


A.4 — Where D2 and D3 land in the RAÍZ flow

The payment, governance, yield and passkey layers already run on testnet. This sprint adds the verifiable transparency link (D2) and the real on-ramp path (D3).

Instawards Statement of Work (SOW)

30-Day Scoped Engagement

Where D2 and D3 land in the RAIZ flow (everything else already runs on testnet)

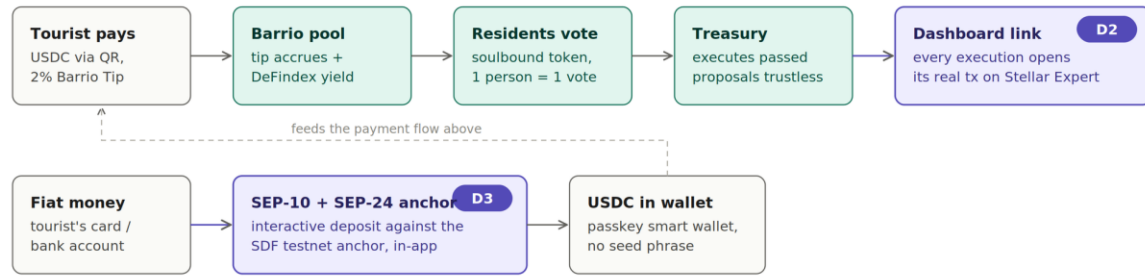

Already live on testnet (not part of this ask):

payments with tip split, soulbound governance, trustless execution, rewards, DeFindex yield, passkey wallets, Mapbox merchant map.
